

KOLIN Philippines International Inc. Survey Form

No: 003726

Customer Name: ANNELO FLORAN

Date: 1-28-20

Address: PHASE 1 95 KATIPUNAN EXT. VICTA HEAL CUKISA

SJR No.: NA/FFI

Establishment Type: Residential ☒

Area Surveyed: LAMA

Commercial ☐

Area Surveyed: _____

Recommended Product Model: KL-1140-GGHIM32

RECOM CUSTOMER CHOICE

Cooling Capacity Computation

Floor Area: 25 sqm.

Ceiling Height: 2.7 mtr.

note: add 20% per meter in excess of 3 meters in the initial cooling capacity computed.

Floor Area: 25

x 550 Btu/h 13,750 Btu/h

Ceiling Height (excess of 3 mtrs.): _____

x 20% _____ Btu/h

Window Direct Sunlight _____

x 100% 20% - 50% 13,750 Btu/h

Total Cooling Capacity _____

27,500 Btu/h

Add : Additional Heat Load

No. of Person 10

x 300 Btu/h 3000 Btu/h

No. of Ordinary Light (<40w) 10

x 200 Btu/h 2000 Btu/h

No. of Special Light (>40w) _____

x 400 Btu/h _____ Btu/h

No. of Refrigerator (< 6 cu.ft.) _____

x 400 Btu/h _____ Btu/h

No. of Refrigerator (> 6 cu.ft.) 1

x 800 Btu/h 800 Btu/h

No. of Cooking Range _____

x 1500 Btu/h _____ Btu/h

No. of Laptop Computer _____

x 150 Btu/h _____ Btu/h

No. of Desktop Computer _____

x 400 Btu/h _____ Btu/h

No. of Printer _____

x 500 Btu/h _____ Btu/h

No. of Photocopier _____

x 1000 Btu/h _____ Btu/h

Total Cooling Capacity _____

5,200 Btu/h

Recommended Cooling Capacity

33,300 Btu/h

Note : Compressor warranty will be reduced to ____ yr. if air-conditioner purchased is lower than the recommended cooling capacity or pipe lay-out is beyond the maximum allowable length.

Scope of Work Agreement

1. Copper tube lay-out

☒

Expose

☐

Embedded

2. Chipping

☐

Included

☒

Not Included

3. Fabricated Bracket

☒

Yes

☐

Shop

☒

Site

☐

No

4. Service Ledge

☒

Yes

☐

No

5. Dismantling of existing Aircon

☐

Included

☒

Not Included

6. Ducting

☐

Yes

☒

No

Dimension : _____


7. Plastering, carpentry and restoration works are to be done by the customer.

8. Wiring of electrical supply from main panel to air-conditioning unit are to be done by the customer.

9. Processing of mechanical plan, working permit, electrical permit are to be done by the customer.

10. Other concern:

CUSTOMER NEED TO PROVIDE TOWEL SHAWL
AT THE OUTDOOR SERVICE. EXPOSE COPPER TUBE
AND ROYAL COND INTO XIES. NEED PLUMBING
AS THROUGH BRACKET, NEED SCREWS. ON SITE
BRACKETED WITH LODGE BRACKET.
NEED WATER OVE TO UNDERCUTTING

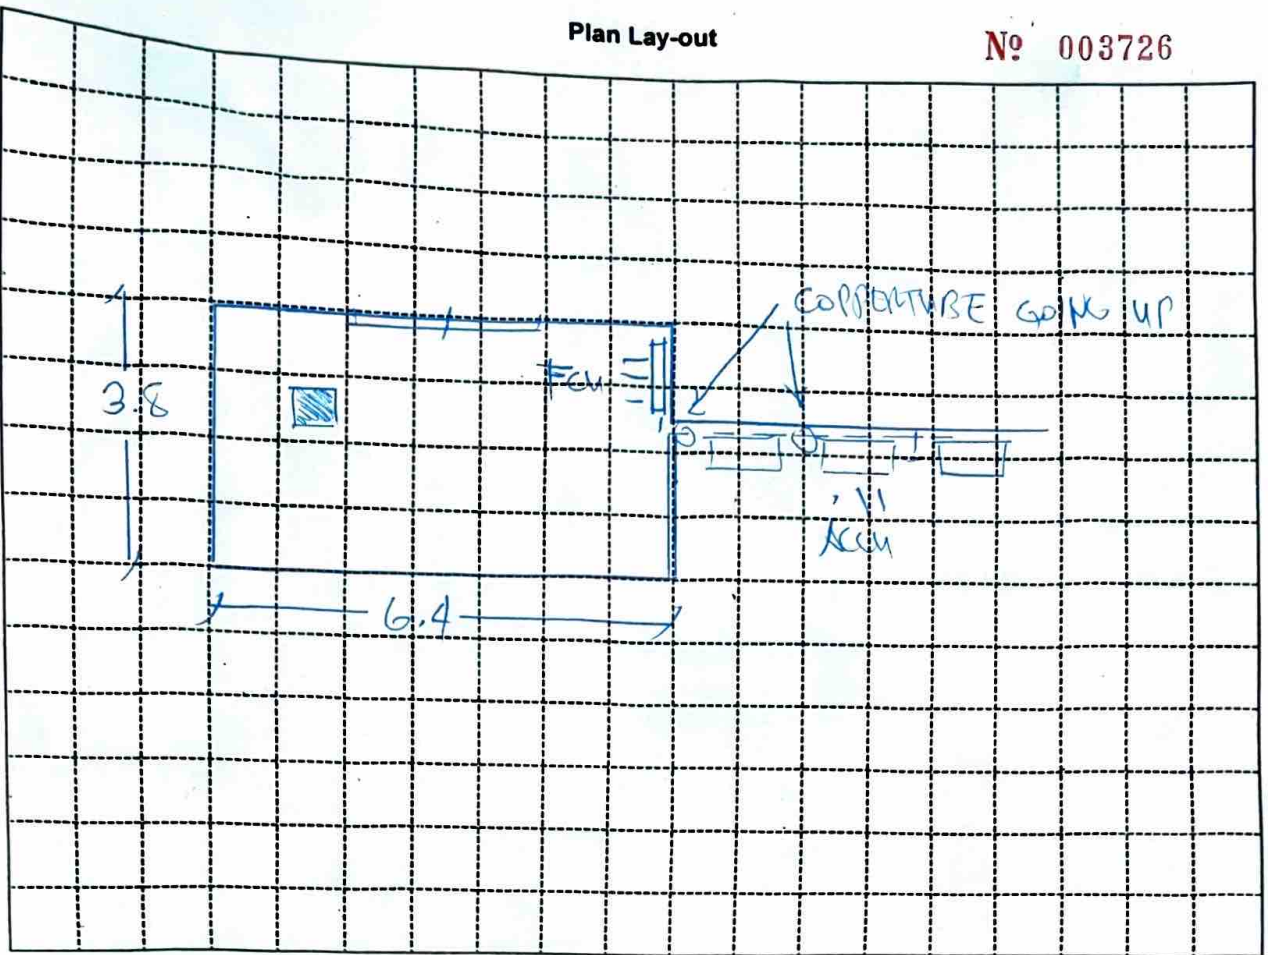

Indoor Unit Location : RIGHT CORNER OF WALL, UP AXES
 Outdoor Unit Location : UP OF AXES IN BETWEEN CR WINDOW, LEVEL OF
 Pipe Length : 20 FT / 6 METERS. TOP OF UNIT AND TOP
 Special Note : OF WINDOW.

Installation Cost Estimate

Material Description	Qty.	Unit Cost	Total Cost
Copper Tube (excess of 10 ft.) 2330, 2430, 2520, 3520, 4620	10 FT	400	4000 ✓
Wire (Royal Cord-signal wire) (excess of 10ft.) 2.0mmx4C	10 FT	100	1000 ✓
Wire (Royal Cord - Breaker to ODU) 3.5mm / 5.5mm x 3C	5 FT	60	300 ✓
Circuit Breaker 20A, 30A, 40A/1ph, 40A/3ph	1	1000	1000 ✓
Bracket (ODU) WITH LEDGE (Imptd. / Fabricated) ; (Floor / Wall)	1	6500	6500 ✓
Bracket (WAC) Angle Type			
PVC Pipe (drain) 1/2" , 3/4"			
PVC Pipe (electrical) 3/4" , 1"			
Drain Pump			
Drain Pump Hose			
Chipping Works 5 CM FLOORING mtr.	2 SETS		1500 ✓
Dismantling Fee (existing air-conditioner)			
Initial Charge LESS OUTDOOR BRACKET (8500 - 800)			7,700 ✓
TOTAL ESTIMATE			P 22,500 ✓

Note :

- Initial Charge includes labor, 10ft. Copper tube, 10ft. Royal cord, Circuit breaker, Outdoor Bracket (SAC), Indoor Bracket (PAC) and Consumable materials.
- Survey fee will be deducted in the installation fee.

Prepared by:

Customer Conforms:

Signature Over Printed Name

Signature Over Printed Name

REVIEWED BY:

01-29-2026
ENGR. ADRIAN NOGOT

Coronica

January 28, 2026

Angelito Elauza

Phase 1, 95 Katipunan Ext. Vista Real Classica Subd. Brgy Batasan Hills, Quezon City
0962-4037259

Please be informed that the air-conditioner you intend to purchase is under capacity as compared to the following unit that we proposed:

Location	Area	Kolin's Recommendation	Customer's Choice	Remarks
LANAI	25 sqm	KL-IF40-6G1M32	KSG-IWF-30WFY8K1M32	Calculated 3.7hp under by 0.7hp

Since the unit of your choice is under capacity, it is probable that you may experience the following;

1. Capacity of the unit to cool the area will take longer or it will not cool the area at all that may lead to your dissatisfaction with the cooling performance of our unit.
2. Power consumption will be higher due to frequent running of compressor for not reaching the desired temperature within the normal parameter.
3. Useful life of compressor will be shortened due to excessive running beyond the normal run cycle.

Considering the above conditions, we regret to inform you that we cannot guarantee the efficient performance of unit. **Also, One (1) year warranty for parts (compressor-3years).**

For your guidance and information


Prepared by:

Jeoffrey T. Dadios
Surveyor

Approved by:


Mr. Alvin de Rivera
Service Manager 1/29/26

Noted by:


Engr. Adrian E. Nogoy
Project Engineer 01-29-2026

Customer Conforme:

Signature Over Printed Name
