

Customer Name : ANLEATO, FLAMPA Date : 1-24-26
 Address : PHASE 1 GC KATIPOPOYAN EXT. VIETA NEAR CURSUA SJR No. : 24/EPD
SPID. 13041 BAYAN BAYAN HILLS, QUEZON CITY

Establishment Type : Residential Area Surveyed : LAMA
 Commercial Area Surveyed : _____

Recommended Product Model : K2-1F40-G6H1M32 (156-1WF-30WF-8K1M32)
RECOM CUSTOMER CHOICE

Cooling Capacity Computation

Floor Area : 25 sqm.
 Ceiling Height : 27 mtr.
 note: add 20% per meter in excess of 3 meters in the initial cooling capacity computed.

Floor Area :	<u>25</u>	x	550 Btu/h	<u>13,750</u> Btu/h
Ceiling Height (excess of 3 mtrs.) :	_____	x	20%	_____ Btu/h
Window Direct Sunlight	_____	x <u>100%</u>	20% - 50%	<u>13,750</u> Btu/h
Total Cooling Capacity	_____			<u>27,500</u> Btu/h

Add : Additional Heat Load

No. of Person	<u>10</u>	x	300 Btu/h	<u>3000</u> Btu/h
No. of Ordinary Light (<40w)	<u>10</u>	x	200 Btu/h	<u>2000</u> Btu/h
No. of Special Light (>40w)	_____	x	400 Btu/h	_____ Btu/h
No. of Refrigerator (< 6 cu.ft.)	_____	x	400 Btu/h	_____ Btu/h
No. of Refrigerator (> 6 cu.ft.)	<u>1</u>	x	800 Btu/h	<u>800</u> Btu/h
No. of Cooking Range	_____	x	1500 Btu/h	_____ Btu/h
No. of Laptop Computer	_____	x	150 Btu/h	_____ Btu/h
No. of Desktop Computer	_____	x	400 Btu/h	_____ Btu/h
No. of Printer	_____	x	500 Btu/h	_____ Btu/h
No. of Photocopier	_____	x	1000 Btu/h	_____ Btu/h
Total Cooling Capacity	_____			<u>5,800</u> Btu/h

Recommended Cooling Capacity 33,300 Btu/h


Note : Compressor warranty will be reduced to ____ yr. if air-conditioner purchased is lower than the recommended cooling capacity or pipe lay-out is beyond the maximum allowable length.

Scope of Work Agreement

- | | | |
|-----------------------------------|---|--|
| 1. Copper tube lay-out | <input checked="" type="checkbox"/> Expose | <input type="checkbox"/> Embedded |
| 2. Chipping | <input type="checkbox"/> Included | <input checked="" type="checkbox"/> Not Included |
| 3. Fabricated Bracket | <input checked="" type="checkbox"/> Yes <input type="checkbox"/> Shop | <input checked="" type="checkbox"/> Site <input type="checkbox"/> No |
| 4. Service Ledge | <input checked="" type="checkbox"/> Yes | <input type="checkbox"/> No |
| 5. Dismantling of existing Aircon | <input type="checkbox"/> Included | <input checked="" type="checkbox"/> Not Included |
| 6. Ducting | <input type="checkbox"/> Yes | <input checked="" type="checkbox"/> No |

Dimension : _____

7. Plastering, carpentry and restoration works are to be done by the customer.
 8. Wiring of electrical supply from main panel to air-conditioning unit are to be done by the customer.
 9. Processing of mechanical plan, working permit, electrical permit are to be done by the customer.
 10. Other concern: CUSTOMER NEED TO PROVIDE POWER SUPPLY AT THE OUTDOOR BRACKET. EXPOSE COPPER TUBE AND ROPE COIL INTO WALL. NEED PLUMBING AS INDOOR BRACKET. NEED SCAFFOLDING - ON SITE. EXPOSED WITH LEDGE BRACKET. NEED WANTED DUE TO UNDERCAPACITY

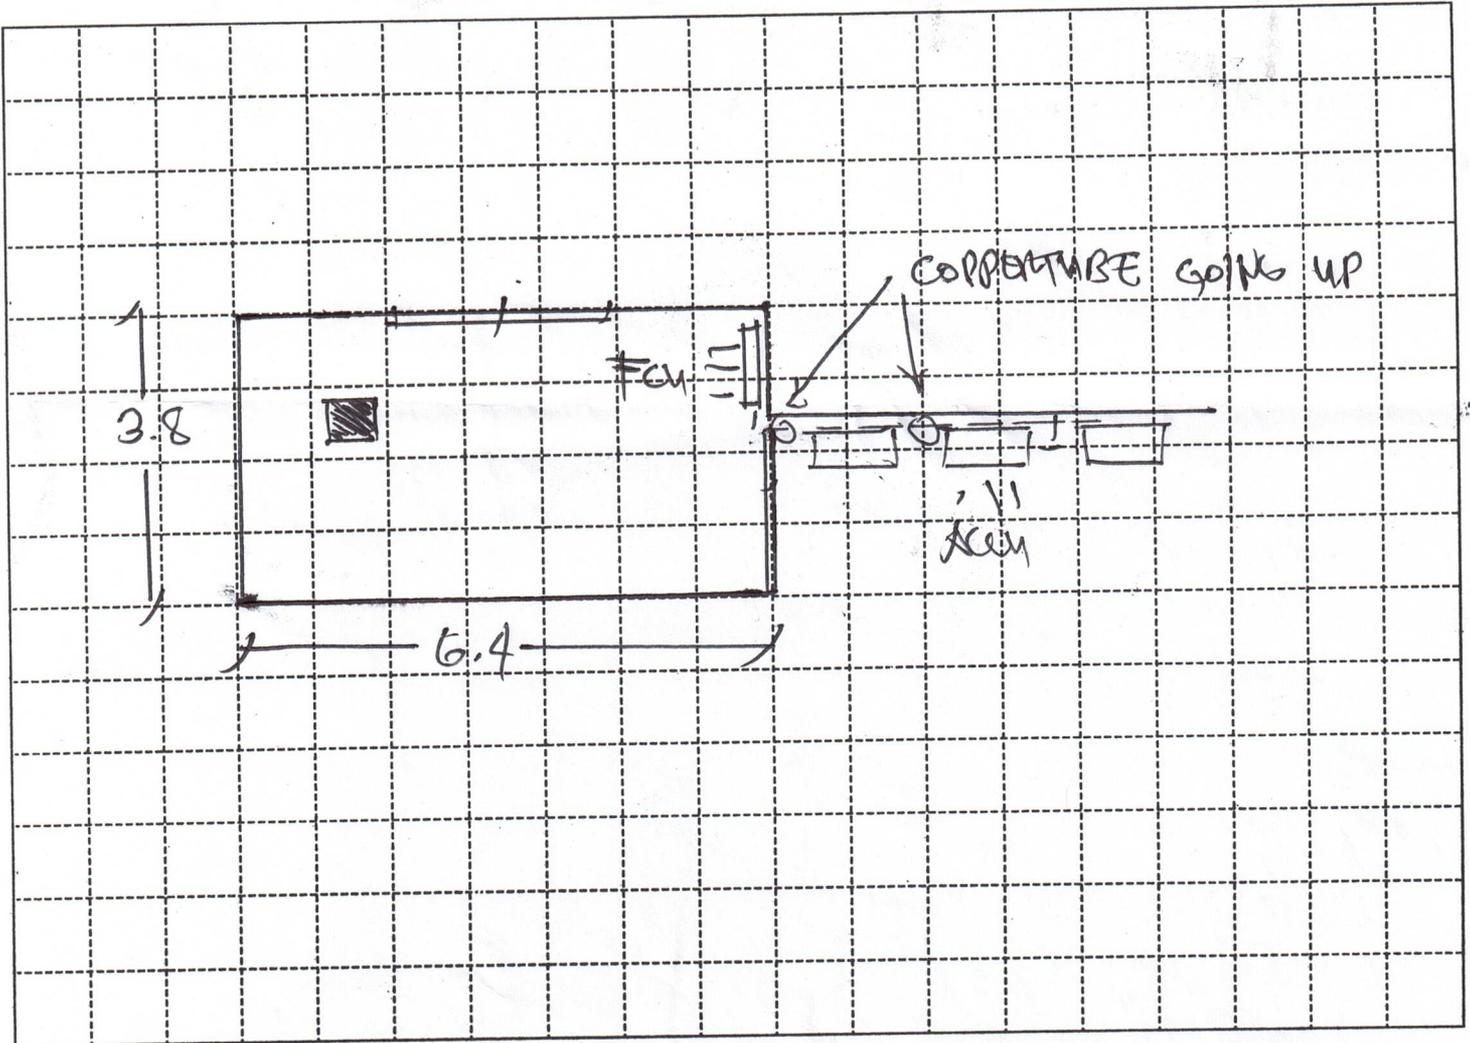

Indoor Unit Location : RIGHT CORNER OF WALL, UP AREA
 Outdoor Unit Location : UP OF AREA IN BETWEEN CR WINDOW LEVEL OF
 Pipe Length : 20 FT / 6 METERS TOP OF UNIT AND TOP OF WINDOW.
 Special Note : _____

Installation Cost Estimate			
Material Description	Qty.	Unit Cost	Total Cost
Copper Tube (excess of 10 ft.)	2330, 2430, 2520, 3520, 4620	10 FT	4000
Wire (Royal Cord-signal wire) (excess of 10ft.)	2.0mmx4C	10 FT	100
Wire (Royal Cord - Breaker to ODU)	3.5mm / 5.5mm x 3C	5 FT	300
Circuit Breaker	20A, 30A, 40A/1ph, 40A/3ph	1	1600
Bracket (ODU) <u>WITH LEDGE</u>	(Imptd. Fabricated) ; (Floor (Wall)	1	6500
Bracket (WAC)	Angle Type		
PVC Pipe (drain)	1/2", 3/4"		
PVC Pipe (electrical)	3/4", 1"		
Drain Pump			
Drain Pump Hose	<u>5 OR FLOW PVC</u> mtr.	25 FT	180
Dismantling Fee (existing air-conditioner)			
Initial Charge	<u>LESS OUTDOOR BRACKET (8,500 - 800)</u>		7,700
TOTAL ESTIMATE			P 22,500

- Note :**
- Initial Charge includes labor, 10ft. Copper tube, 10ft. Royal cord, (Outdoor Bracket (SAC), Indoor Bracket (PAC) and Consumable materials.
 - Survey fee will be **deducted** in the installation fee.

Prepared by:

 Signature Over Printed Name

Customer Conforme:

 Signature Over Printed Name
 Jones Coronica
