

KOLIN Philippines International Inc.
Survey Form

No 003493

Customer Name : HENRY XNG Date : 7-11-24
 Address : ESSEX HILLS MOUNTAIN HILLS SUBD. SJR No. : 42250
NEW MANILA, P.C.
 Establishment Type : Residential ☒ Area Surveyed : GUESTROOM
 Commercial ☐ Area Surveyed : _____
 Recommended Product Model : KSM-1WN-WCT10W/1H32

Cooling Capacity Computation

Floor Area : 16 sqm.
 Ceiling Height : 2.5 mtr.

note: add 20% per meter in excess of 3 meters in the initial cooling capacity computed.

Floor Area :	<u>16</u>	x	550 Btu/h	<u>8800</u>	Btu/h
Ceiling Height (excess of 3 mtrs.) :		x	20%		Btu/h
Window Direct Sunlight		x	20% - 50%	<u>1760</u>	Btu/h
Total Cooling Capacity				<u>10560</u>	Btu/h

Add : Additional Heat Load

No. of Person	<u>2</u>	x	300 Btu/h	<u>600</u>	Btu/h
No. of Ordinary Light (<40w)	<u>4</u>	x	200 Btu/h	<u>800</u>	Btu/h
No. of Special Light (>40w)		x	400 Btu/h		Btu/h
No. of Refrigerator (< 6 cu.ft.)		x	400 Btu/h		Btu/h
No. of Refrigerator (> 6 cu.ft.)		x	800 Btu/h		Btu/h
No. of Cooking Range		x	1500 Btu/h		Btu/h
No. of Laptop Computer		x	150 Btu/h		Btu/h
No. of Desktop Computer		x	400 Btu/h		Btu/h
No. of Printer		x	500 Btu/h		Btu/h
No. of Photocopier		x	1000 Btu/h		Btu/h
Total Cooling Capacity				<u>1400</u>	Btu/h

Recommended Cooling Capacity

1400 Btu/h
1.3
11960 Btu/h

Note : Compressor warranty will be reduced to ____ yr. if air-conditioner purchased is lower than the recommended cooling capacity or pipe lay-out is beyond the maximum allowable length.


Scope of Work Agreement

- | | | |
|-----------------------------------|--|--|
| 1. Copper tube lay-out | ☒ Expose | ☐ Embedded |
| 2. Chipping | ☐ Included | ☒ Not Included |
| 3. Fabricated Bracket | ☐ Yes ☐ Shop | ☐ Site ☒ No |
| 4. Service Ledge | ☐ Yes | ☒ No |
| 5. Dismantling of existing Aircon | ☐ Included | ☒ Not Included |
| 6. Ducting | ☐ Yes | ☒ No |

Dimension : _____

7. Plastering, carpentry and restoration works are to be done by the customer.
 8. Wiring of electrical supply from main panel to air-conditioning unit are to be done by the customer.
 9. Processing of mechanical plan, working permit, electrical permit are to be done by the customer.
 10. Other concern: CUSTOMER TRANSFER POWER SUPPLY TO THE

CHASSIS LOCATION
WORKING DAYS: 8AM-5PM: MONDAY - SATURDAY
CUSTOMER CONTINGENT NEED TO CUT THE
CORNER TO FIT THE UNIT
OUTDOOR USE 1P 24VX2

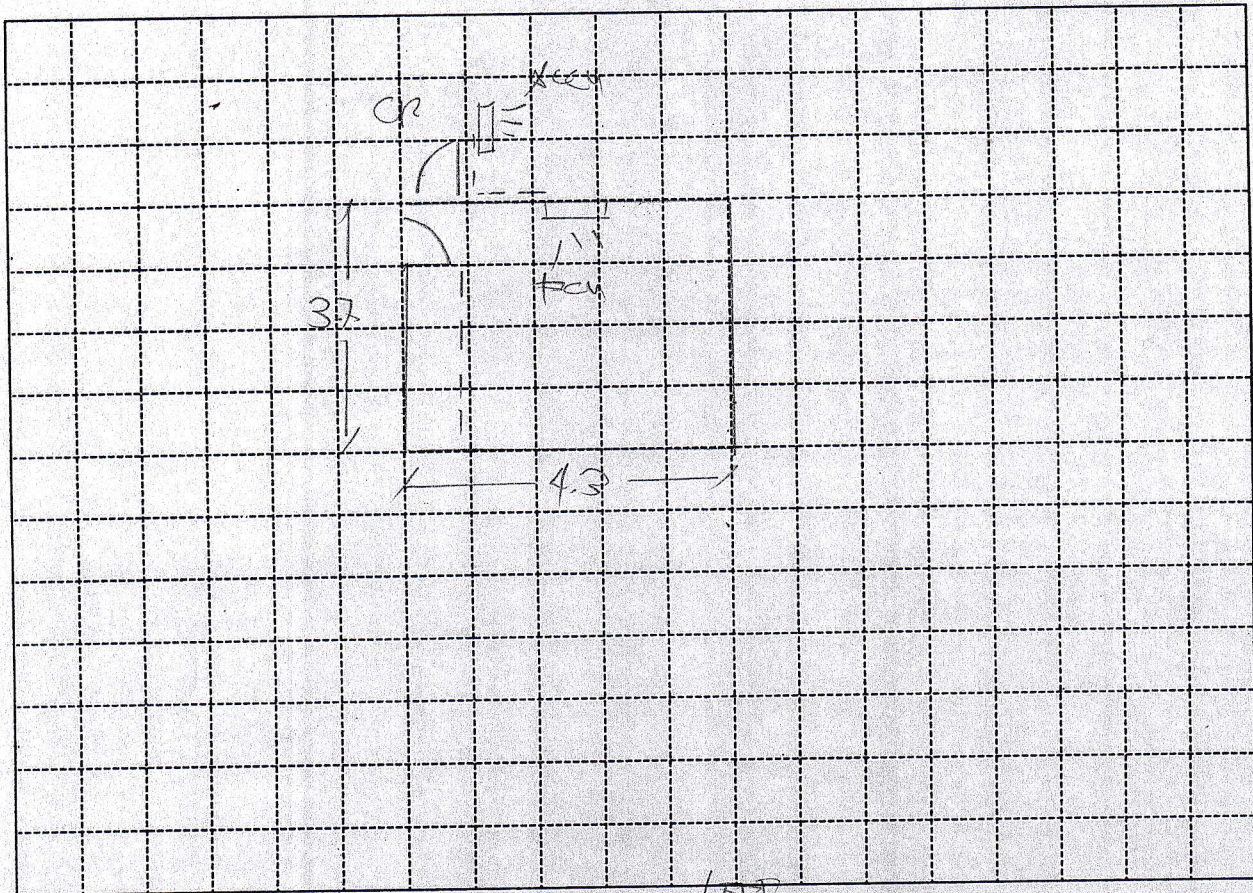

Indoor Unit Location :

WP OF WINDOW, RIGHT CORNER

Outdoor Unit Location :

AT THE CR WALL

Pipe Length :

10 FT

Special Note :

Installation Cost Estimate

Material Description	Qty.	Unit Cost	Total Cost
Copper Tube (excess of 10 ft.)	2330, 2430, 2520, 3520, 4620		
Wire (Royal Cord-signal wire) (excess of 10ft.)	2.0mmx4C	700	700
Wire (Royal Cord - Breaker to ODU)	3.5mm / 5.5mm x 3C	60	420
Circuit Breaker	20A, 30A, 40A/1ph, 40A/3ph	1000	1000
Bracket (ODU)	(Imptd./ Fabricated) ; (Floor / Wall)		
Bracket (WAC)	Angle Type		
PVC Pipe (drain)	1/2" & 3/4"	150	150
PVC Pipe (electrical)	3/4", 1"		
Drain Pump			
Drain Pump Hose	WATER 1/2"	125	125
Chipping Works	mtr.		
Dismantling Fee (existing air-conditioner)			1500
Initial Charge			
TOTAL ESTIMATE		P 9,945	

Note :

- Initial Charge includes labor, 10ft. Copper tube, 10ft. Royal cord, Circuit breaker, Outdoor Bracket (SAC), Indoor Bracket (PAC) and Consumable materials.
- Survey fee will be **deducted** in the installation fee.

Prepared by:

Signature Over Printed Name

Customer Conforme:

Signature Over Printed Name
