

KOLIN Philippines International Inc.
Survey Form

No. 003573

Customer Name : CAN KANG S&Y CO SOCIETY INC Date : 1-14-25
 Address : 1398 NAYAN ST. B267 741 TATUBAN MANILA SJR No. : 237835

Establishment Type : Residential ☐ Area Surveyed :
 Commercial ☒ Area Surveyed : Meeting Room

Recommended Product Model : KSG-300K1F (OLD UNIT)

Cooling Capacity Computation

Floor Area : 42 sqm.
 Ceiling Height : 2.1 mtr.

note: add 20% per meter in excess of 3 meters in the initial cooling capacity computed.

Floor Area :	<u>42</u>	x	550 Btu/h	<u>23,100</u> Btu/h
Ceiling Height (excess of 3 mtrs.) :		x	20%	
Window Direct Sunlight		x	20% - 50%	
Total Cooling Capacity				<u>23,100</u> Btu/h

Add : Additional Heat Load

No. of Person	<u>10</u>	x	300 Btu/h	<u>3000</u> Btu/h
No. of Ordinary Light (<40w)	<u>10</u>	x	200 Btu/h	<u>2000</u> Btu/h
No. of Special Light (>40w)		x	400 Btu/h	
No. of Refrigerator (< 6 cu.ft.)		x	400 Btu/h	
No. of Refrigerator (> 6 cu.ft.)		x	800 Btu/h	
No. of Cooking Range		x	1500 Btu/h	
No. of Laptop Computer		x	150 Btu/h	
No. of Desktop Computer		x	400 Btu/h	
No. of Printer		x	500 Btu/h	
No. of Photocopier		x	1000 Btu/h	
Total Cooling Capacity				<u>5800</u> Btu/h

Recommended Cooling Capacity 28,900 Btu/h

Note : Compressor warranty will be reduced to ____ yr. if air-conditioner purchased is lower than the recommended cooling capacity or pipe lay-out is beyond the maximum allowable length.


Scope of Work Agreement

- | | | |
|-----------------------------------|--|--|
| 1. Copper tube lay-out | ☒ Expose | ☐ Embedded |
| 2. Chipping | ☐ Included | ☒ Not Included |
| 3. Fabricated Bracket | ☐ Yes ☐ Shop | ☐ Site ☒ No |
| 4. Service Ledge | ☐ Yes | ☒ No |
| 5. Dismantling of existing Aircon | ☐ Included | ☐ Not Included |
| 6. Ducting | ☐ Yes | ☒ No |

Dimension :

- Plastering, carpentry and restoration works are to be done by the customer.
- Wiring of electrical supply from main panel to air-conditioning unit are to be done by the customer.
- Processing of mechanical plan, working permit, electrical permit are to be done by the customer.
- Other concern: RELOCATION OF OUTDOOR ONLY.

REMOVE COPPER TUBE AND COMMUNICATION WIRES.
NEW HOLE TO THE LEFT OF 1 PDSH UNIT
CUSTOMER NEED TO TRANSFER POWER SUPPLY TO
OUTDOOR NEW LOCATION. 4 PAX, BRING HAMMER
AND ROPE. Use existing outdoor bracket & breaker
Existing outdoor bracket to be spot weld on new location.

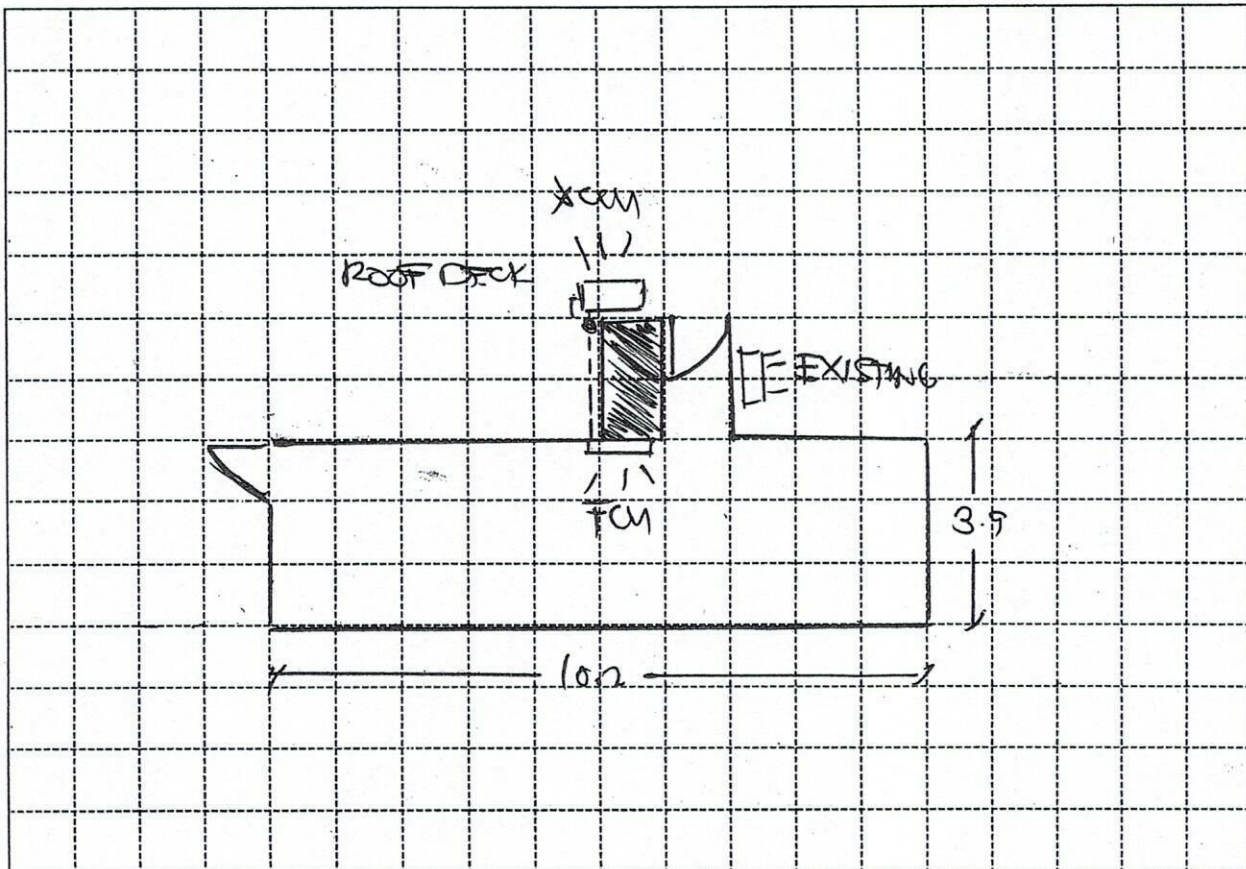

Indoor Unit Location : SAME LOCATION
 Outdoor Unit Location : AT THE ROOF DECK
 Pipe Length : 12 METERS / 40 FT
 Special Note : _____

Installation Cost Estimate			
Material Description	Qty.	Unit Cost	Total Cost
Copper Tube (excess of 10 ft.) 2330, 2430, <u>2520</u> , 3520, 4620	<u>40 FT</u>	<u>400</u>	<u>16000</u>
Wire (Royal Cord-signal wire) (excess of 10ft.) 2.0mmx4C	<u>47 FT</u>	<u>100</u>	<u>4700</u>
Wire (Royal Cord - Breaker to ODU) 3.5mm / 5.5mm x 3C			
Circuit Breaker 20A, 30A, 40A/1ph, 40A/3ph			
Bracket (ODU) (Imptd. / Fabricated) ; (Floor / Wall)			
Bracket (WAC) Angle Type			
PVC Pipe (drain) 1/2", 3/4"			
PVC Pipe (electrical) 3/4", 1"			
Drain Pump			
Drain Pump Hose			
Chipping Works mtr.			
Dismantling Fee (existing air-conditioner)			
Initial Charge <u>DISMANTLE AND RELOCATE OUTDOOR.</u>			<u>4300</u>
TOTAL ESTIMATE		P 25,000 -	

Note :

- Initial Charge includes labor, 10ft. Copper tube, 10ft. Royal cord, Circuit breaker, Outdoor Bracket (SAC), Indoor Bracket (PAC) and Consumable materials.
- Survey fee will be **deducted** in the installation fee.

Prepared by:

JEFFREY 03/10/15
 Signature Over Printed Name

Customer Conforme:

Signature Over Printed Name
