

KOLIN Philippines International Inc.
Survey Form

Nº 003605

Customer Name : LYDIA ECHAVEZ Date : 3-6-78
 Address : 836 104th ST. ADDITION HILLS, WINDSOR, ONT. CAN. SJR No. : 247206

Establishment Type : Residential ☒ Commercial ☐ Area Surveyed : TV Room
 Area Surveyed : _____

Recommended Product Model : KXG-250WCIHV (2 PCS)

Cooling Capacity Computation

Floor Area : 52 sqm.
 Ceiling Height : 2.9 mtr.

note: add 20% per meter in excess of 3 meters in the initial cooling capacity computed.

Floor Area :	<u>52</u>	x	550 Btu/h	<u>28600</u>	Btu/h
Ceiling Height (excess of 3 mtrs.) :		x	20%		Btu/h
Window Direct Sunlight		x	20% - 50%	<u>5720</u>	Btu/h
Total Cooling Capacity				<u>34320</u>	Btu/h

Add : Additional Heat Load

No. of Person	<u>13</u>	x	300 Btu/h	<u>3900</u>	Btu/h
No. of Ordinary Light (<40w)	<u>10</u>	x	200 Btu/h	<u>2000</u>	Btu/h
No. of Special Light (>40w)		x	400 Btu/h		Btu/h
No. of Refrigerator (< 6 cu.ft.)		x	400 Btu/h		Btu/h
No. of Refrigerator (> 6 cu.ft.)		x	800 Btu/h		Btu/h
No. of Cooking Range		x	1500 Btu/h		Btu/h
No. of Laptop Computer		x	150 Btu/h		Btu/h
No. of Desktop Computer <u>1</u>	<u>1</u>	x	400 Btu/h	<u>400</u>	Btu/h
No. of Printer		x	500 Btu/h		Btu/h
No. of Photocopier		x	1000 Btu/h		Btu/h
Total Cooling Capacity				<u>7800</u>	Btu/h

Recommended Cooling Capacity

42120 Btu/h


Note : Compressor warranty will be reduced to ____ yr. if air-conditioner purchased is lower than the recommended cooling capacity or pipe lay-out is beyond the maximum allowable length.

Scope of Work Agreement

- | | | |
|-----------------------------------|--|---|
| 1. Copper tube lay-out | ☐ Expose | ☐ Embedded |
| 2. Chipping | ☐ Included | ☐ Not Included |
| 3. Fabricated Bracket | ☐ Yes ☐ Shop | ☐ Site ☐ No |
| 4. Service Ledge | ☐ Yes | ☐ No |
| 5. Dismantling of existing Aircon | ☐ Included | ☐ Not Included |
| 6. Ducting | ☐ Yes | ☐ No |

Dimension :

- Plastering, carpentry and restoration works are to be done by the customer.
- Wiring of electrical supply from main panel to air-conditioning unit are to be done by the customer.
- Processing of mechanical plan, working permit, electrical permit are to be done by the customer.
- Other concern; HOLE EXISTING (66 cm x 43 cm)

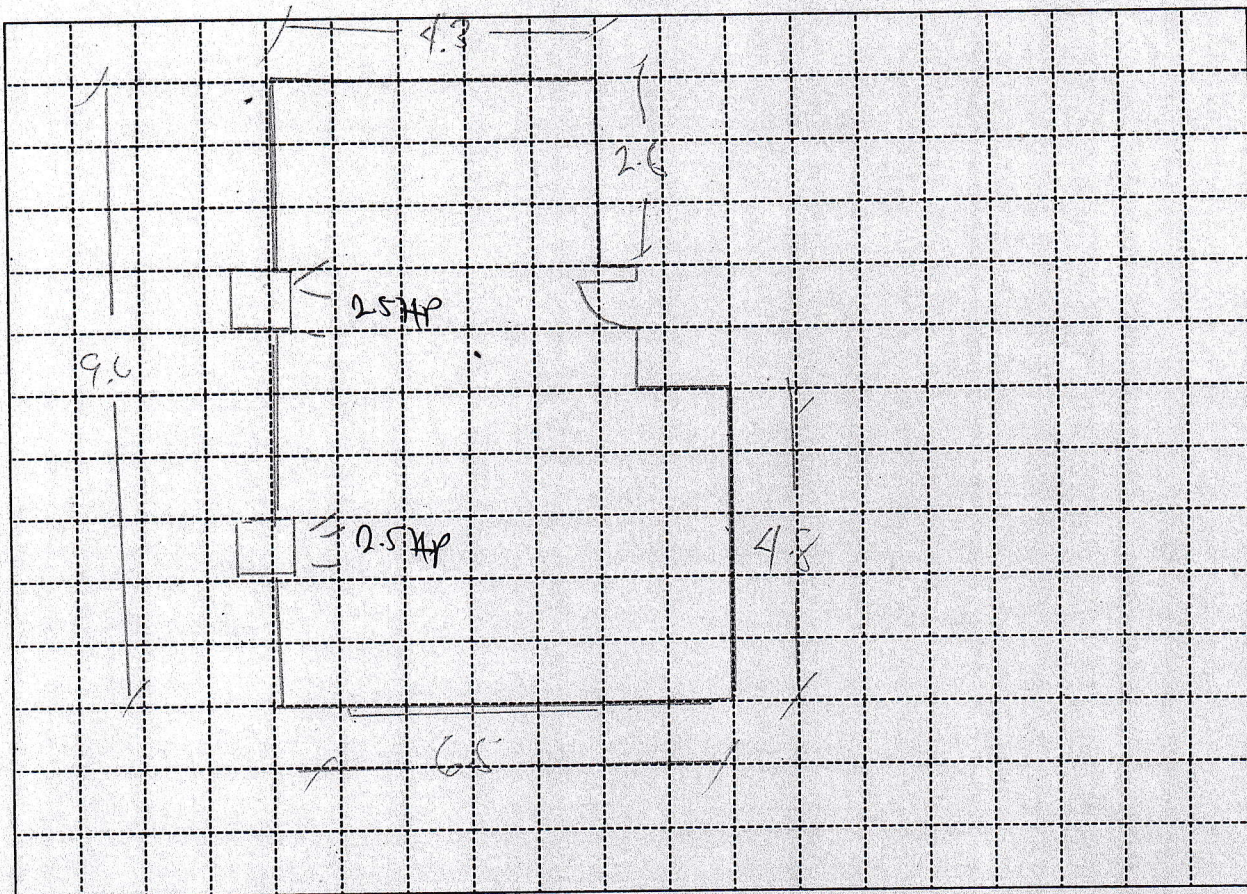

Indoor Unit Location :

Outdoor Unit Location :

Pipe Length :

Special Note :

WINDOW TYPE (2 PCS)

Installation Cost Estimate

Material Description	Qty.	Unit Cost	Total Cost
Copper Tube (excess of 10 ft.) 2330, 2430, 2520, 3520, 4620			
Wire (Royal Cord-signal wire) (excess of 10ft.) 2.0mmx4C			
Wire (Royal Cord - Breaker to ODU) 3.5mm / 5.5mm x 3C			
Circuit Breaker 20A, 30A, 40A/1ph, 40A/3ph			
Bracket (ODU) (Imptd. / Fabricated) ; (Floor / Wall)			
Bracket (WAC) Angle Type	2 PCS	600	1200
PVC Pipe (drain) 1/2", 3/4"			
PVC Pipe (electrical) 3/4", 1"			
Drain Pump			
Drain Pump Hose			
Chipping Works mtr.			
Dismantling Fee (existing air-conditioner)			
Initial Charge	2 PCS	1200	2400
TOTAL ESTIMATE		P 3600 -	

Note :

- Initial Charge includes labor, 10ft. Copper tube, 10ft. Royal cord, Circuit breaker, Outdoor Bracket (SAC), Indoor Bracket (PAC) and Consumable materials.
- Survey fee will be **deducted** in the installation fee.

Prepared by:

Signature Over Printed Name

Customer Conforme:

Signature Over Printed Name
