

KOLIN Philippines International Inc.
Survey Form

No 003449

Customer Name: JESSE JANSSEN MANOZ Date: 5-3-24
 Address: 35 PINKETIA ST. TATBADA VILLAGE BT SJR No.: 19661
HOMES, PASAY CITY
 Establishment Type: Residential ☒ Area Surveyed: MASTER BEDROOM
 Commercial ☐ Area Surveyed: _____
 Recommended Product Model: KSM 1WK - W9TOMIM32

Cooling Capacity Computation

Floor Area: 32.5 sqm.
 Ceiling Height: 2.9 mtr.

note: add 20% per meter in excess of 3 meters in the initial cooling capacity computed.

Floor Area:	<u>32.5</u>	x	550 Btu/h	<u>17875</u> Btu/h
Ceiling Height (excess of 3 mtrs.):	<u>2.9</u>	x	20%	_____ Btu/h
Window Direct Sunlight		x	20% - 50%	_____ Btu/h
Total Cooling Capacity				<u>17875</u> Btu/h

Add : Additional Heat Load

No. of Person	<u>2</u>	x	300 Btu/h	<u>600</u> Btu/h
No. of Ordinary Light (<40w)	<u>5</u>	x	200 Btu/h	<u>1000</u> Btu/h
No. of Special Light (>40w)	_____	x	400 Btu/h	_____ Btu/h
No. of Refrigerator (< 6 cu.ft.)	_____	x	400 Btu/h	_____ Btu/h
No. of Refrigerator (> 6 cu.ft.)	_____	x	800 Btu/h	_____ Btu/h
No. of Cooking Range	_____	x	1500 Btu/h	_____ Btu/h
No. of Laptop Computer	_____	x	150 Btu/h	_____ Btu/h
No. of Desktop Computer <u>1</u>	<u>1</u>	x	400 Btu/h	<u>400</u> Btu/h
No. of Printer	_____	x	500 Btu/h	_____ Btu/h
No. of Photocopier	_____	x	1000 Btu/h	_____ Btu/h
Total Cooling Capacity				<u>2000</u> Btu/h

Recommended Cooling Capacity

2.2
19875 Btu/h

Note : Compressor warranty will be reduced to ____ yr. if air-conditioner purchased is lower than the recommended cooling capacity or pipe lay-out is beyond the maximum allowable length.


Scope of Work Agreement

- | | | |
|-----------------------------------|--|--|
| 1. Copper tube lay-out | ☒ Expose | ☐ Embedded |
| 2. Chipping | ☐ Included | ☒ Not Included |
| 3. Fabricated Bracket | ☐ Yes ☐ Shop | ☐ Site ☒ No |
| 4. Service Ledge | ☐ Yes | ☒ No |
| 5. Dismantling of existing Aircon | ☒ Included | ☐ Not Included |
| 6. Ducting | ☐ Yes | ☒ No |

Dimension : _____

- Plastering, carpentry and restoration works are to be done by the customer.
- Wiring of electrical supply from main panel to air-conditioning unit are to be done by the customer.
- Processing of mechanical plan, working permit, electrical permit are to be done by the customer.
- Other concern: DISMANTLE AND INSTALL NEW COPPER TUBE, OUTDOOR
BRACKET AND BRACKET. PROTECT ADDRESS AND
ROPE. 4 PAX.
EXPLORE COPPER TUBE W/ DISMANTLE IN THE X-REF.

WHT

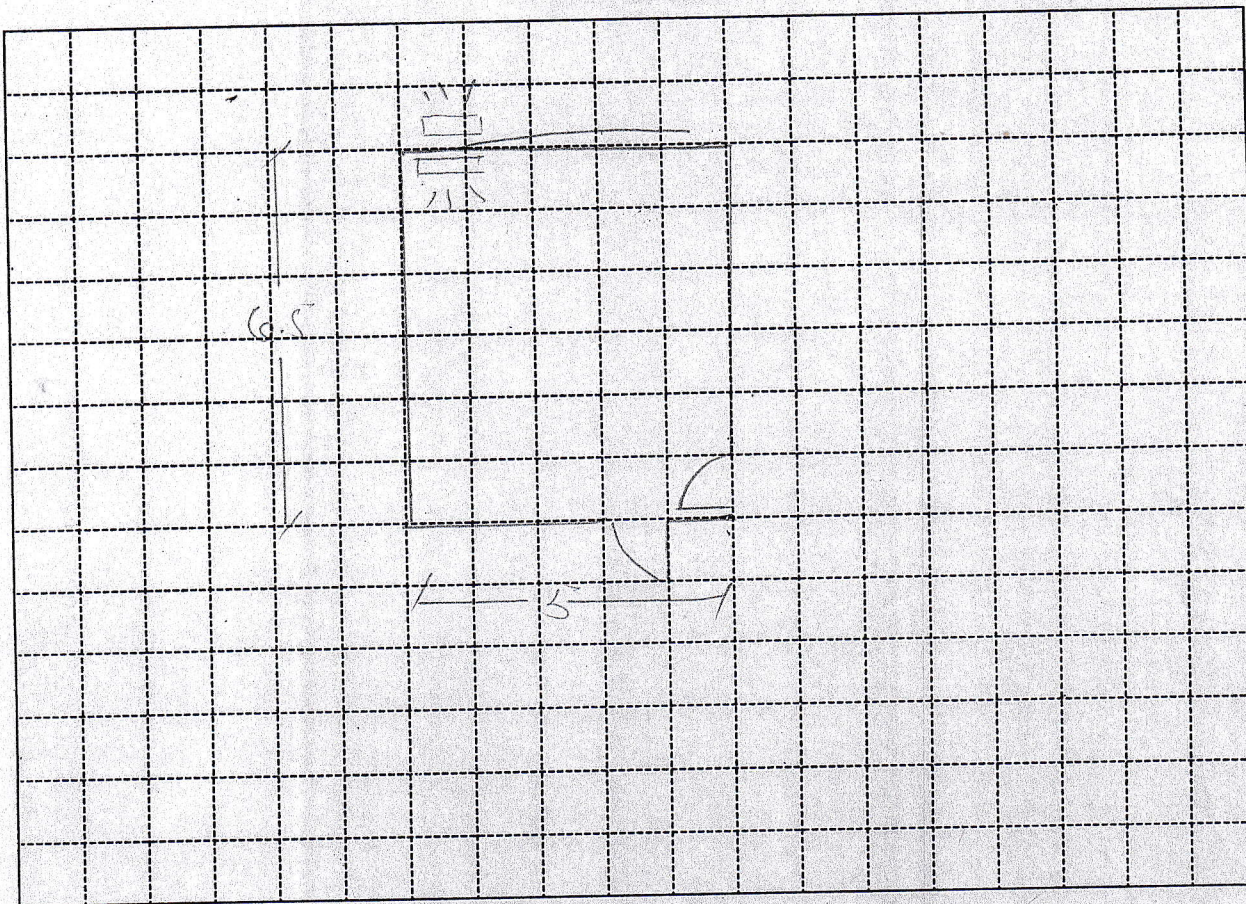

Indoor Unit Location : SKINE LOCATION, LEFT CORNER W3U
 Outdoor Unit Location : AT THE BACK UP OF COPY
 Pipe Length : 4 METERS / 14 FT
 Special Note :

Installation Cost Estimate			
Material Description	Qty.	Unit Cost	Total Cost
Copper Tube (excess of 10 ft.) 2330, 2430, 2520, 3520, 4620	4 FT	400	1600
Wire (Royal Cord-signal wire) (excess of 10ft.) 2.0mmx4C	1 FT	100	100
Wire (Royal Cord - Breaker to ODU) 3.5mm / 5.5mm x 3C	4 FT	60	240
Circuit Breaker 20A, 30A, 40A/1ph, 40A/3ph	1	1000	1000
Bracket (ODU) (Imptd. / Fabricated) : (Floor / Wall)			
Bracket (WAC) Angle Type			
PVC Pipe (drain) 1/2", 3/4"	1	150	150
PVC Pipe (electrical) 3/4", 1"			
Drain Pump			
Drain Pump Hose WHITE 1/2"	7 FT	25	175
Chipping Works mtr.			2500
Dismantling Fee (existing air-conditioner) 2.5 HP			850
Initial Charge			
TOTAL ESTIMATE		P 15,265	

Note :

- Initial Charge includes labor, 10ft. Copper tube, 10ft. Royal cord, Circuit breaker, Outdoor Bracket (SAC), Indoor Bracket (PAC) and Consumable materials.
- Survey fee will be deducted in the installation fee.

Prepared by:

Signature Over Printed Name

Customer Conforms:

Signature Over Printed Name
