

KOLIN Philippines International Inc.
Survey Form

No 003534

Customer Name : CLXMISSX OMATION Date : 9-13-24
 Address : 11-312 BXVYXP BLDG. MERCEDES XE SJR No. : 422035
LNR ST. EAST 10515 DAWWENS, DILIG SAN MIGUEL, P.S. 16
 Establishment Type : Residential ☒ Area Surveyed : DINING, LIVING, KITCHEN
 Commercial ☐ Area Surveyed :

Recommended Product Model : KSM-10N20-WCT10M/M32 (KSM-10N20-WCT10M/M32)
PER AN INDICATION CUSTOMER CHOICE

Cooling Capacity Computation

Floor Area : 19.2 sqm.
 Ceiling Height : 2.4 mtr.

note: add 20% per meter in excess of 3 meters in the initial cooling capacity computed.

Floor Area :	<u>19.2</u>	x	550 Btu/h	<u>10560</u> Btu/h
Ceiling Height (excess of 3 mtrs.) :		x	20%	
Window Direct Sunlight		x	20% - 50%	
Total Cooling Capacity				<u>10560</u> Btu/h

Add : Additional Heat Load

No. of Person	<u>4</u>	x	300 Btu/h	<u>1200</u> Btu/h
No. of Ordinary Light (<40w)	<u>5</u>	x	200 Btu/h	<u>1000</u> Btu/h
No. of Special Light (>40w)		x	400 Btu/h	
No. of Refrigerator (< 6 cu.ft.)	<u>1</u>	x	400 Btu/h	<u>400</u> Btu/h
No. of Refrigerator (> 6 cu.ft.)		x	800 Btu/h	
No. of Cooking Range	<u>1</u>	x	1500 Btu/h	<u>1500</u> Btu/h
No. of Laptop Computer	<u>1</u>	x	150 Btu/h	<u>150</u> Btu/h
No. of Desktop Computer	<u>1</u>	x	400 Btu/h	<u>400</u> Btu/h
No. of Printer		x	500 Btu/h	
No. of Photocopier	<u>1</u>	x	1000 Btu/h	<u>1000</u> Btu/h
Total Cooling Capacity				<u>16210</u> Btu/h

Recommended Cooling Capacity

Note : Compressor warranty will be reduced to ____ yr. if air-conditioner purchased is lower than the recommended cooling capacity or pipe lay-out is beyond the maximum allowable length.


Scope of Work Agreement

- | | | |
|-----------------------------------|--|--|
| 1. Copper tube lay-out | ☒ Expose | ☐ Embedded |
| 2. Chipping | ☐ Included | ☒ Not Included |
| 3. Fabricated Bracket | ☐ Yes ☐ Shop | ☐ Site ☒ No |
| 4. Service Ledge | ☐ Yes | ☒ No |
| 5. Dismantling of existing Aircon | ☐ Included | ☒ Not Included |
| 6. Ducting | ☐ Yes | ☒ No |

Dimension : _____

- Plastering, carpentry and restoration works are to be done by the customer.
- Wiring of electrical supply from main panel to air-conditioning unit are to be done by the customer.
- Processing of mechanical plan, working permit, electrical permit are to be done by the customer.
- Other concern;

EXPLORE COPPER TUBE IF THE XRAY, N/D/10/11/12
CUSTOMER NEED TO PROVIDE POWER SUPPLY
AT THE OUTDOOR, 5/10/11/12
NEED WORKING PERMIT. 3 DAY.

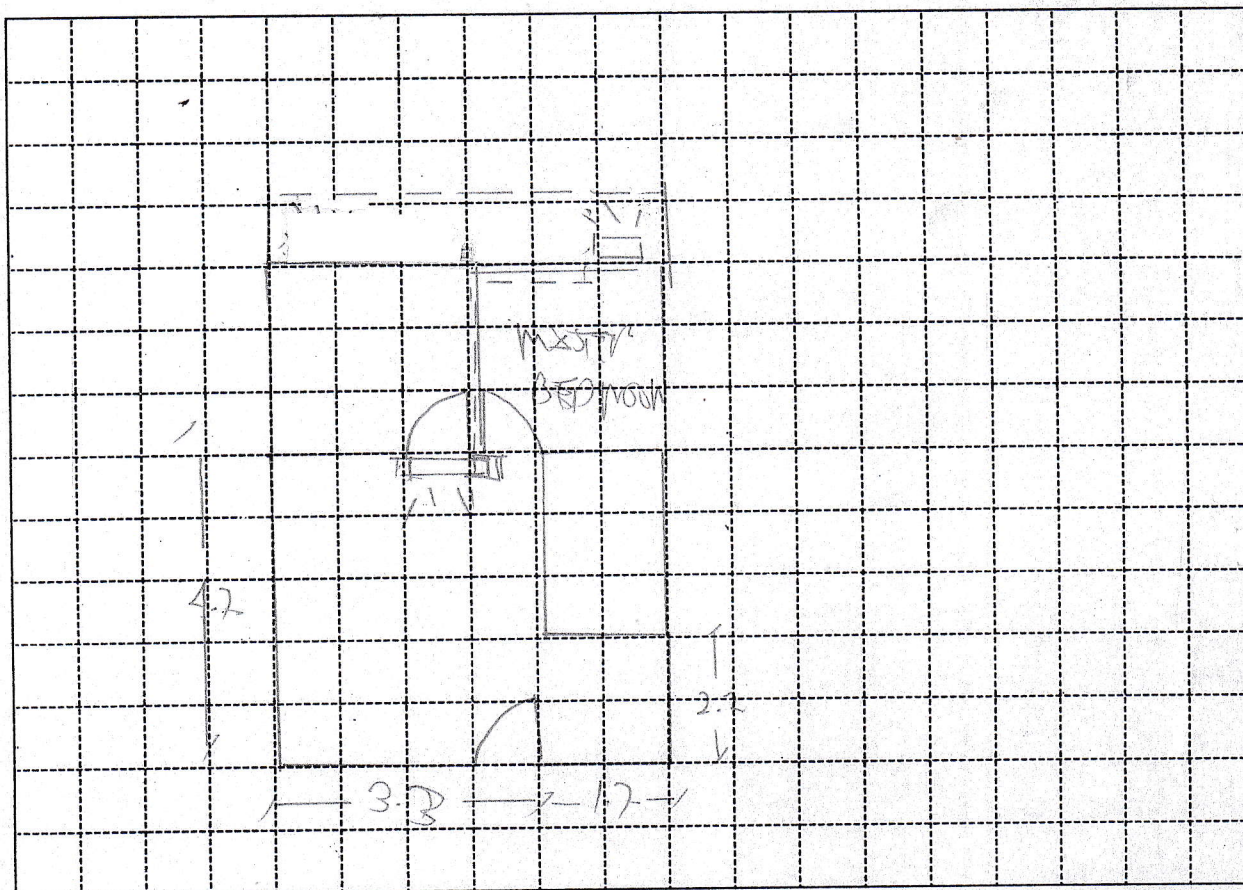

Indoor Unit Location : UP OF TWO DOOR,
 Outdoor Unit Location : BELOW OF WINDOW TYPE, MASTER
 Pipe Length : 22 FT
 Special Note :

Installation Cost Estimate			
Material Description	Qty.	Unit Cost	Total Cost
Copper Tube (excess of 10 ft.) 2330, 2430, 2520, 3520, 4620	12 FT	350	4200
Wire (Royal Cord-signal wire) (excess of 10ft.) 2.0mmx4C	15 FT	100	1500
Wire (Royal Cord - Breaker to ODU) 3.5mm / 5.5mm x 3C	2 FT	60	120
Circuit Breaker 20A, 30A, 40A/1ph, 40A/3ph	1	1000	1000
Bracket (ODU) (Imptd. / Fabricated) ; (Floor / Wall)			
Bracket (WAC) Angle Type			
PVC Pipe (drain) 1/2" , 3/4"	2 Pcs	150	300
PVC Pipe (electrical) 3/4" , 1"			
Drain Pump			
Drain Pump Hose WHP 1/2"	75	25	175
Chipping Works mtr.			
Dismantling Fee (existing air-conditioner)			
Initial Charge			7580
QUOTATION FOR (2HP)		TOTAL ESTIMATE	P 15,495-

Note :

1. Initial Charge includes labor, 10ft. Copper tube, 10ft. Royal cord, Circuit breaker, Outdoor Bracket (SAC), Indoor Bracket (PAC) and Consumable materials.
2. Survey fee will be **deducted** in the installation fee.

Prepared by:

Signature Over Printed Name

Customer Conforme:

Signature Over Printed Name
