

GODSPEED REFRIGERATION AND AIRCONDITIONING SERVICES

Customer Name : DANIEL ONG
 Address : NORTH PARKVIEW
 Establishment Type: Residential ☒ Commercial ☐
 Area Surveyed : MASTER Bedroom 2
 Date : NOV 16 2020
 SJR No : _____

Cooling Capacity Computation

note: add 20% per meter in excess of 3 meters in the initial cooling capacity computed.

Floor Area : 24.5 sqm.
 Ceiling Height : _____ mtr.

Floor Area : 24.5
 Ceiling Height (excess of 3 mtrs.) : _____

Windows Direct Sunlight

Glass Wall Direct Sunlight

Total Cooling Capacity

Add : Additional Heat Load

No. of Person

No. of Ordinary Light (<40w)

No. of Special Light (<40w)

No. of Refrigerator (<6 cu.ft.)

No. of Refrigerator (<6 cu.ft.)

No. of Television

No. of Cooking Range

No. of Laptop Computer

No. of Desktop Computer

No. of Printer

No. of Photocopier

Total Cooling Capacity

Computed Cooling Capacity

Recommended Product Model KSM1W20

Recommended Capacity / Type 2HP

Note : Compressor warranty will be reduced to _____ yr. If air-conditioner purchased is lower than the recommended cooling capacity or pipe lay-out is beyond the maximum allowable length.

Scope of Agreement

1. Copper tube lay-out

2. Chipping

3. Fabricated bracket

4. Service Ledge

5. Dismantling of existing Aircon

5. Leak Test of existing Copper tube

7. Duct works

8. Location of indoor and outdoor units were agreed by the customer and surveyor.

9. Plastering, Carpentry and restoration works are to be done by the customer.

10. Wiring of electrical supply from main panel to air-conditioning unit are to be done by the customer.

11. Processing of mechanical plan, working permit are to be done by the customer.


12. Other concern;

CALLING TYPE

☒ Expose	☐ Embedded
☐ Included	☐ Not Included
☐ Yes	☐ No
☐ Yes	☐ No
☐ Included	☐ c/o Customer
☐ Yes	☐ No
☐ Yes	☐ No

13,475	Btu/h
	Btu/h
	Btu/h
	Btu/h
	Btu/h
	Btu/h
600	Btu/h
	Btu/h
1200	Btu/h
	Btu/h
	Btu/h
400	Btu/h
	Btu/h
	Btu/h
	Btu/h
	Btu/h
	Btu/h
15,675	Btu/h
2HP	HP

Plan Lay-out

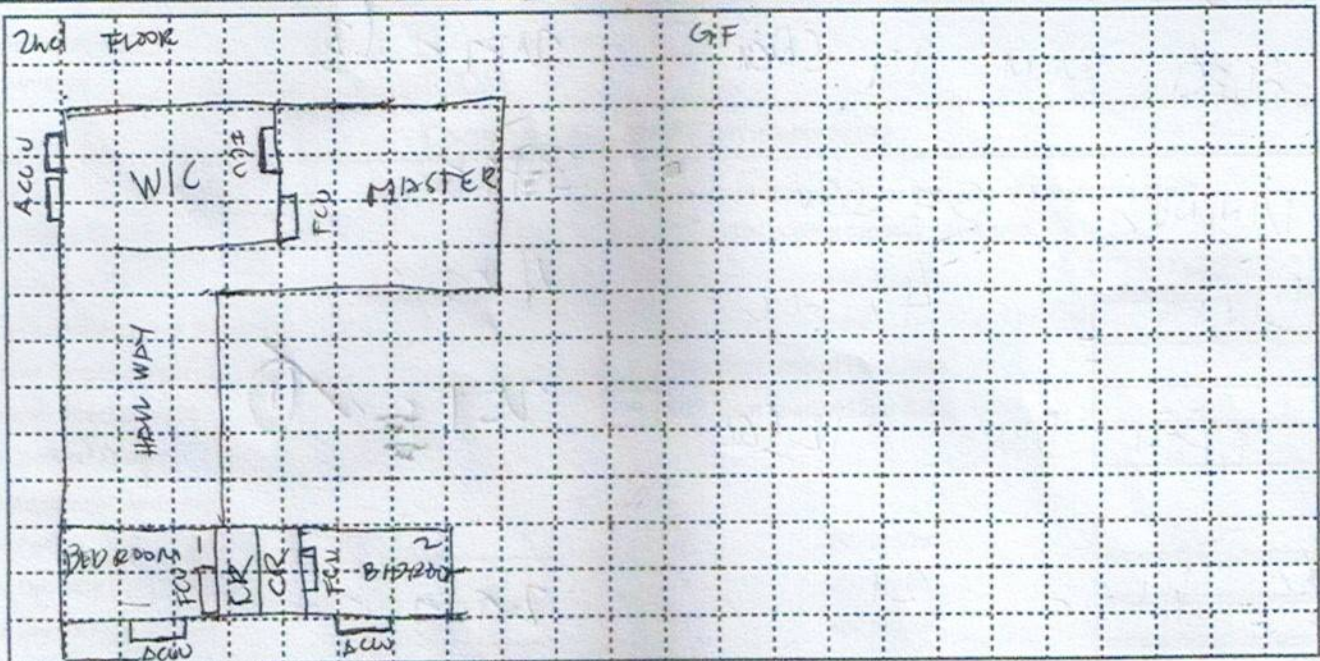

Indoor Unit Location : MASTER'S BEDROOM 2
 Outdoor Unit Location : _____
 Pipe Length : 35 FT.
 Special Note : HANG BRACKET

Instruction : ☐ Encircle required specifications (copper tube size, power supply, circuit breaker and ODU bracket)

Installation Cost Estimate

Material Description	Qty.	Unit Cost	Total Cost
Insu. Copper Tube (Excess of 10ft.) <u>3/8" x 1/4" 1/2" x 1/4" 5/8" x 1/4" 5/8" x 3/8" 7/8" x 3/8"</u>	<u>25</u>	<u>P 300</u>	<u>P 8700</u>
Communication Wire - Royal Cord (Excess 10ft.) 2.0sqmm x 4c	<u>30</u>	<u>100</u>	<u>3000</u>
Power Supply - Royal Cord (Breaker to ODU) 3.5sqmm x 3c 5.5sqmm x 3c 8.0sqmm x 3c			
Circuit Breaker 20Amps/1Ph <u>30Amps/1Ph</u> 40Amps/Ph 60Amps/1Ph 40Amps/3Ph 100Amps/3Ph			<u>1000</u>
Bracket (ODU) Kolin Wall Kolin Floor Fab. Floor Fab. Wall Fab. Wall w/ ledge			
Angel Bracket (WAC)			
PVC Pipe (Drain) 3/4" x 10' 1" x 10'			<u>150</u>
Leaktest Existing Copper Tube (Ø dia ____ x ____, estimated length ____ ft)			
Dismantling Fee (Existing Air-Conditioning unit capacity ____ HP)			
Chipping Works			
Others _____			
Initial Charge			<u>P 8.50</u>
TOTAL ESTIMATE			<u>P 21.40</u>

Note:

- Final charges will be based on actual installation.
- Survey fee will be deducted in the installation fee.

Prepared by:

Customer Conforms:

Signature Over Printed Name

Signature Over Printed Name
